

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION



STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1111
TRUNK HIGHWAY 84
COUNTY Cass
DISTRICT 3A

LIMITS: Jct. T.H. 87 at Pontoria - Jct. T.H. 200

Ref. Pt. 011+00.292 - 030+00.036

YEAR BUILT	PROJECT N ^o	DESCRIPTION				CODE N ^o
		TYPE	WIDTH	THICKNESS	REMARKS	
C	1111-06	Plant Mix Bit.	24'	1 1/2" Added		1
C	A.F.E. 836	Guard Rail			2028'	2
M	A.F.E. 604	Bit. Surf. Repair	24'		SC-3, 58838 Gal. Agg. 4869 Tons	3
M		Bit. Surf. Repair	22'		MG3&MG269988 Gal.	4
1960		Light Bit. Seal	24'		RS-1, 7593 Gal. Agg. 289 C.Y.	
M	C	Light Bit. Seal	23'		RS-2K, 21114 Gal. Agg. 826 C.Y.	5
M	C	Light Bit. Seal	25'		CRS-1 Bit. 8480 Gal. FA-1 Agg. 306 C.Y.	6
C	1111-09	Bit SURFACING Agg. SHOULDERS & Misc GRAZING	23' 24'	1 1/2" or Bit. Pass		7
C	1111-12	Bit. Overlay Gravel Shoulder	24' 3'	2 1/2" 2 1/2"	Spec. 2350 Class 1	8
C	1111-10	Grading Bit. Overlay	32' 24'		Spec. 2350	9
M	8823-41	Bit. Route and Seal			Spec. 3725	10
D	D06077 8823-85	Bit. Seal Coat	24'		Spec. 2356	11
S	1111-13	Grading/Agg. base Bit. Surfacing Remove Br. 984, 1103	48' 44'	6" 6"	Spec. 2360	12
S	1111-16	Bit. Mill & Overlay ML & TL's & shldr-parking	var var	2" 2"	Spec. 2360 rumble strips CL	13

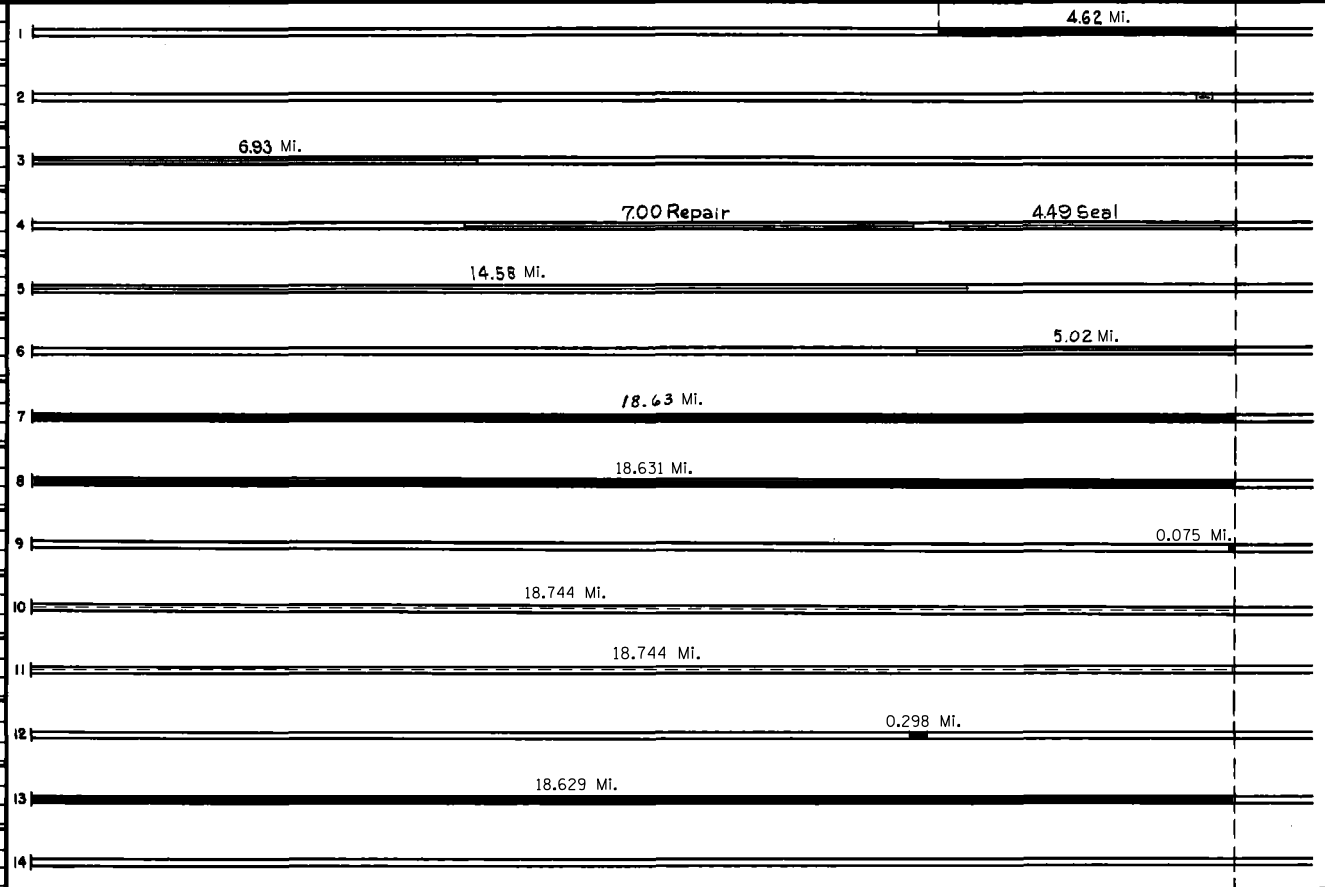

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.

REMARKS: See Sheet No. 1
