


PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 3607  
TRUNK HIGHWAY 46  
COUNTY Koochiching  
DISTRICT 2A

LIMITS: Jct. T.H. 1 in Northome - S. Co. Line



YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N° DIST.
		TYPE	WIDTH	THICKNESS	
					No Record of Constr.
		Gravel	14'	2"	
					Added in 1894.
C	3607-02	Clearing			By W.P.A. On new line.
C	3607-01	Grading Stab. Gravel	30'		1200 C.Y. / MI. 2+1
C	A.F.E. 7	Seeding			Seed supplied by R.S.D. (S.P. 3607-03) Maint. Dept.
M	1948 A.F.E. 6	Grav. Resurfacing			1156 Tons
C	3607-05	Grading Stab. Gravel	30x2 26x2	9"	3+8
C	A.F.E. 70 A.F.E. 7	Bit Surfacing Mixed Bit. Seeding	28x0	1"	MC 3, 3730 Gal. Agg. 220 C.Y.
M	1950 A.F.E. 6	Gravel Resurfacing			874 Tons
C	3607-07	Sand-Grav. Sub-base Gravel Base Mixed Bit.	30' 28x2 24x2	6" 2'-3"	1.54 Mi. of Sub-base 1051
M	1954 A.F.E. 605	Light Bit. Seal	28x8		RS-1 & MC 2, 2848 Gal. Agg. 120 C.Y.
C	3607-10				957
C	3607-09	Plant Mix Bit.	26x0 24x2 added		957
M	1962	Light Bit Seal	25'		RS-2, 3458 Gal. Agg. 120 C.Y. 1262
C	1975 3607-11	Pl. Mix Bit. Resurf. Gravel Shoulders	24' 3'	1 1/2" VAR.	LAST 0.0366 MI. IS S4 SURF. WIDTH 175
C	1979 3600-12	THREE CABLE GUARD RAIL AT M.P. 44.9			100 LIN. FT.

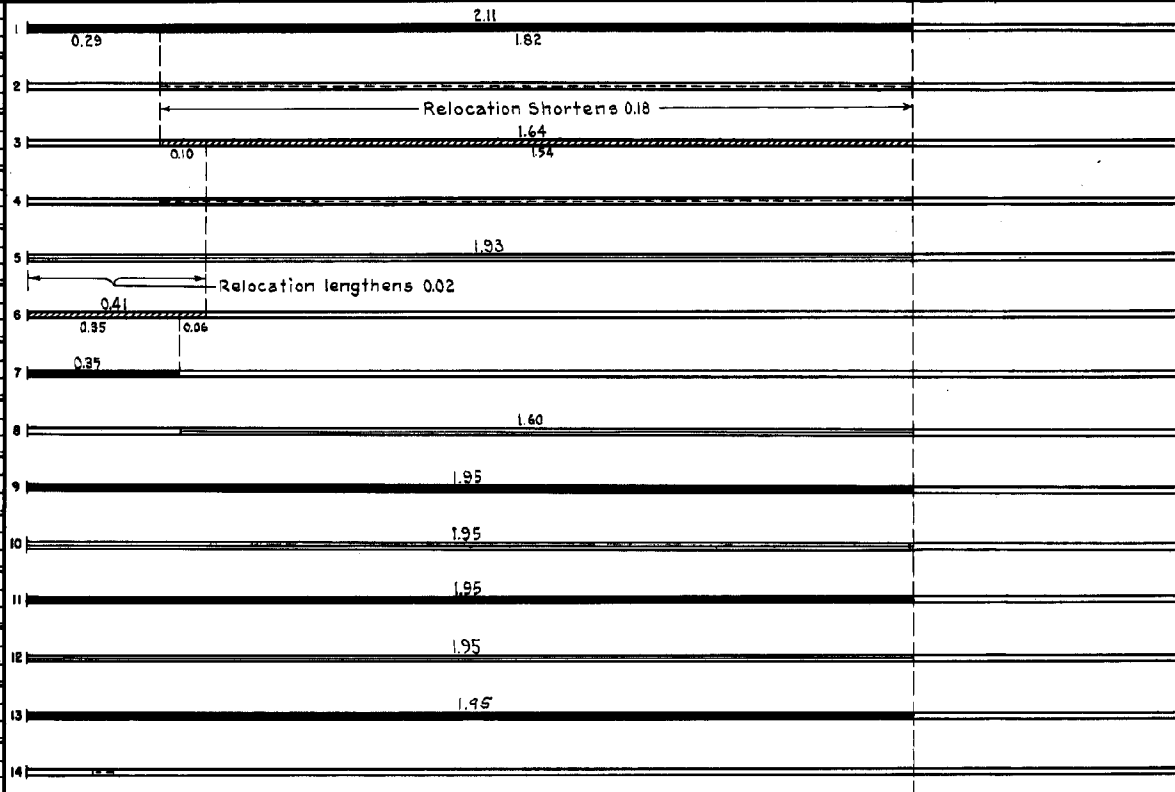

YEARS FROM	TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
			RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1940	2.11	1.77	0.00	0.34	0.00	2.11	0.00	0.00	0.00
1941	1948	1.93	1.60	0.00	0.33	0.00	1.93	0.00	0.00	0.00
1949		1.95	1.61	0.00	0.34	0.00	1.95	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1941

