

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6109
TRUNK HIGHWAY 104
COUNTY Pope
DISTRICT 4B

LIMITS: S. Co. Line - Jct. C.S.A.H. 29 (W. End of Curve)

Ref. Pt. 018+00.435 - 025+00.059

Swift Co.
Pope
Kandiyohi Co.



PLAN


C.S.A.H. 104

C.S.A.H. 104



SCALE: 1 MI.

YEAR BUILT	PROJECT N°	DESCRIPTION		CODE N°
		TYPE	WIDTH THICKNESS	
				No Record of Constr.
		Gravel	20' 1 1/2"	Added in 1934
C 1941	A.F.E. 43 A.F.E. 59	Grading & Culv. Seeding		Seeds supplied by R.S.D. (S.P. 6109-03) Maint. Dept.
C 1941	A.F.E. 58	Gravel		640 C.Y./Mile. Maint. Dept.
M 1941	A.F.E. 58	Spot Graveling		260 C.Y./Mile. Maint. Dept.
M 1945	A.F.E. 6	Grav. Resurfacing		342 C.Y./Mi. Maint. Dept.
M 1946	A.F.E. 30	Grade Lift	24' 3.0'	3010 C.Y.
M 1951	A.F.E. 6	Grav. Resurfacing (Spot)		822 C.Y.
M 1952	A.F.E. 6	Grav. Resurfacing		816 C.Y. & 294 Tons
C 1954	6109-07	Grading Gravel	30' 3 3/4" 26' 1 1/2"	700 C.Y./Mi.
C 1955	6109-08	Stab. Sand-Gr. Sub-base Stab. Gravel Base Plant Mix Bit.	30' 0'-6" 30' 3" 24' 1 1/2"	
M 1956	A.F.E. 605	Bit. Seal Coat	24'	RC-5, 25455 Gal. Agg. 714 C.Y.
M 1963		Light Bit. Seal	25'	RS-2K, 12140 Gal. Agg. 412 C.Y.
M 1990	4381	Bit. Overlay Bit. Shouldering	24' 1 1/2" 2' 1 1/2"	Spec 2341
M 2003	8824-39	Bit. Seal Coat	28'	FA-3

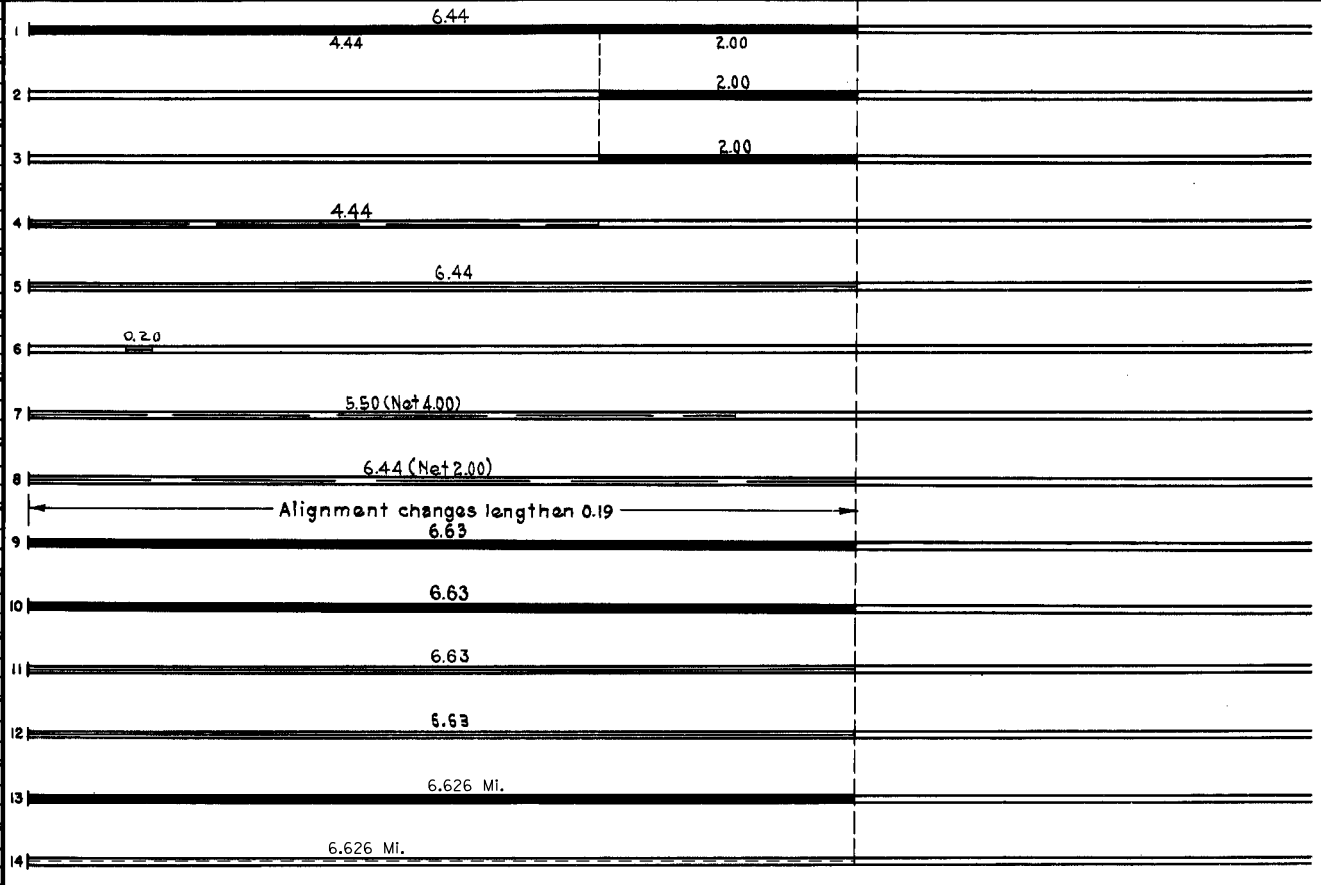

YEARS		TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
FROM	TO		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1934	1953	6.44	6.44	0.00	0.00	0.00	0.00	6.44	0.00	0.00
1954		6.63	6.63	0.00	0.00	0.00	0.00	6.63	0.00	0.00

REMARKS: Layout is to scale as of 1934

