

PREPARED BY  
HIGHWAY PLANNING SURVEY  
IN COOPERATION WITH  
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA  
DEPARTMENT OF HIGHWAYS  
ROAD LIFE STUDIES  
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 6409  
TRUNK HIGHWAY 273  
COUNTY Redwood  
DISTRICT 8B

LIMITS: Jct. T.H. 19 - N. Jct. CSAH 9 in Belview

Ref. Pt. 000+00.000 - 005+00.023

YEAR BUILT	PROJECT N°	DESCRIPTION			CODE N°
		TYPE	WIDTH	THICK-NESS	
		Gravel Bridge 3825	38.38	27	No Record of Const. Added in 1949
		Mixed Bit.	24		No Record of Const. Added in 1949
M	1949 A.F.E. 6	Grav. Resurfacing			3248 Tons
C	1952 6409-02	Grading (4.79 Mi.) Grav. Base (4.79 Mi.) Mixed Bit.	28' 28'	9-12"	* Resurf. center 26' of 50-60 rdwy. from Mi. Pt. 4.25-4.48
C	1953 A.F.E. 907	Seeding			
M	1953 A.F.E. 605	Light Bit. Seal	24'		AERS-2, 8718 Gal. Agg. 413 Tons
M	1958 A.F.E. 604	Spot Treat Bit. Surf. Repair	24'		MC-2, 5900 Gal. Agg. 378 Tons
M	1961	Spot Treat Bit. Surf. Repair	24'		SC-3 & MC-2, 8400 Gal. for Repair & 1332 Gal. for tack
M	1962	Spot Treat Bit. Surf. Repair	24'		SC-3, 10140 Gal. Bit. Material 791 tons
C	1974 -04	Grading Gravel Base Pl. Mix Bit. Surf.	24'		
M	1996 6409-96105	Milling Bit. Overlay	24' 24'	1 1/2" 1 1/2"	Spec. 2341
S	2001 6409-06	Milling Bit. Overlay Gravel Shoulder	24' 24' 6'	1 1/2" 1 1/2" 2.00	Spec. 2350 Class 1

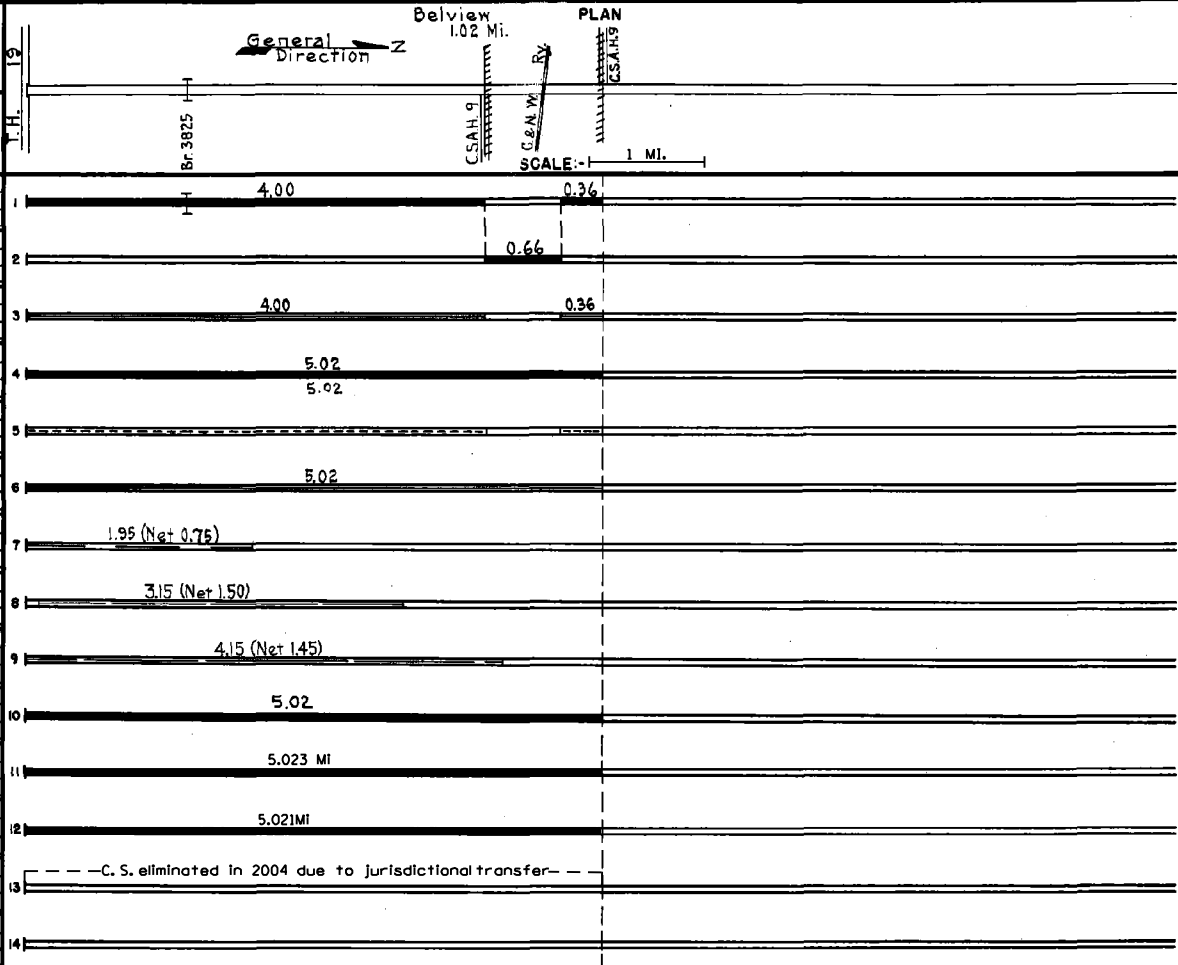

YEARS FROM	TOTAL MILES TO	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949	5.02	3.99	0.01	1.02	0.00	2.01	0.01	0.00	0.00

REMARKS: Layout is to scale as of 1949
