


PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U.S. PUBLIC ROADS ADMINISTRATION


STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1310
TRUNK HIGHWAY 243
COUNTY Chicago
DISTRICT Metro

LIMITS: Jct. T.H. 93 - W. End of St. Croix River Bridge (E. Co. Line)
Ref. Pt. 000+00.000 - 001+00.163



YEAR BUILT	PROJECT N°	DESCRIPTION				CODE N°
		TYPE	WIDTH	THICKNESS	REMARKS	
		Gravel	28'		No Record of Const. Added in 1949	
C	1949 A.F.E. 4#40	Bit Surfacing Bit Surf-Treated	20'	3 1/2"	MC2#3, 5941 Gal Agg. 100 C.Y.	
C	1950 A.F.E. 30	Bit Resurfacing Mixed Bit.	21'	1 1/2" added	RT-6, 5501 Gal. Agg. 324 C.Y.	
C	1952 A.F.E. 21 A.F.E. 39	Bit Resurfacing Mixed Bit. Install C.M. Culvs	24'	1 1/2" added	RT-6, 8280 Gal. Agg. 699 Tons Fill Washouts	
C	1953 A.F.E. 625 A.F.E. 830 *	Grading Bit Stab. Sand-Grav. Mixed Bit.	36' 30'	12" Var.	MC2&RT-6, 22800 Gal. Agg. 1211 Tons * Guard Rail	
C	1954 A.F.E. 825	Bit Resurfacing Plant Mix Bit. Bit Seal Coat	24 1/2'	1 1/2" added	Bit. 15426 Gal. Agg. 1391 Tons	
C	1956 1310-04	Plant Mix Bit.	24 1/2'	4" 5" added		
M	1958 A.F.E. 605	Bit Seal Coat	Var.		RS-2, 2785 Gal. Agg. 95 C.Y.	
M	1964 C	Light Bit. Seal	24'		RS-2K, 2025 Gal. Agg. 81 C.Y.	
C	1978 1310-09	Bit. RESURFACING & SHOULDER	24'	1 1/2"		
	1992 M4564	Mill & Bit. Overlay	25'	2"	Spec 2331, 2361	
S	2008 1310-13	Bit. Seal Coat			Types FA-2 & FA-3	
	2010 1310-12	Milling Bit. Overlay	24'	4" 4"	Spec. 2360	

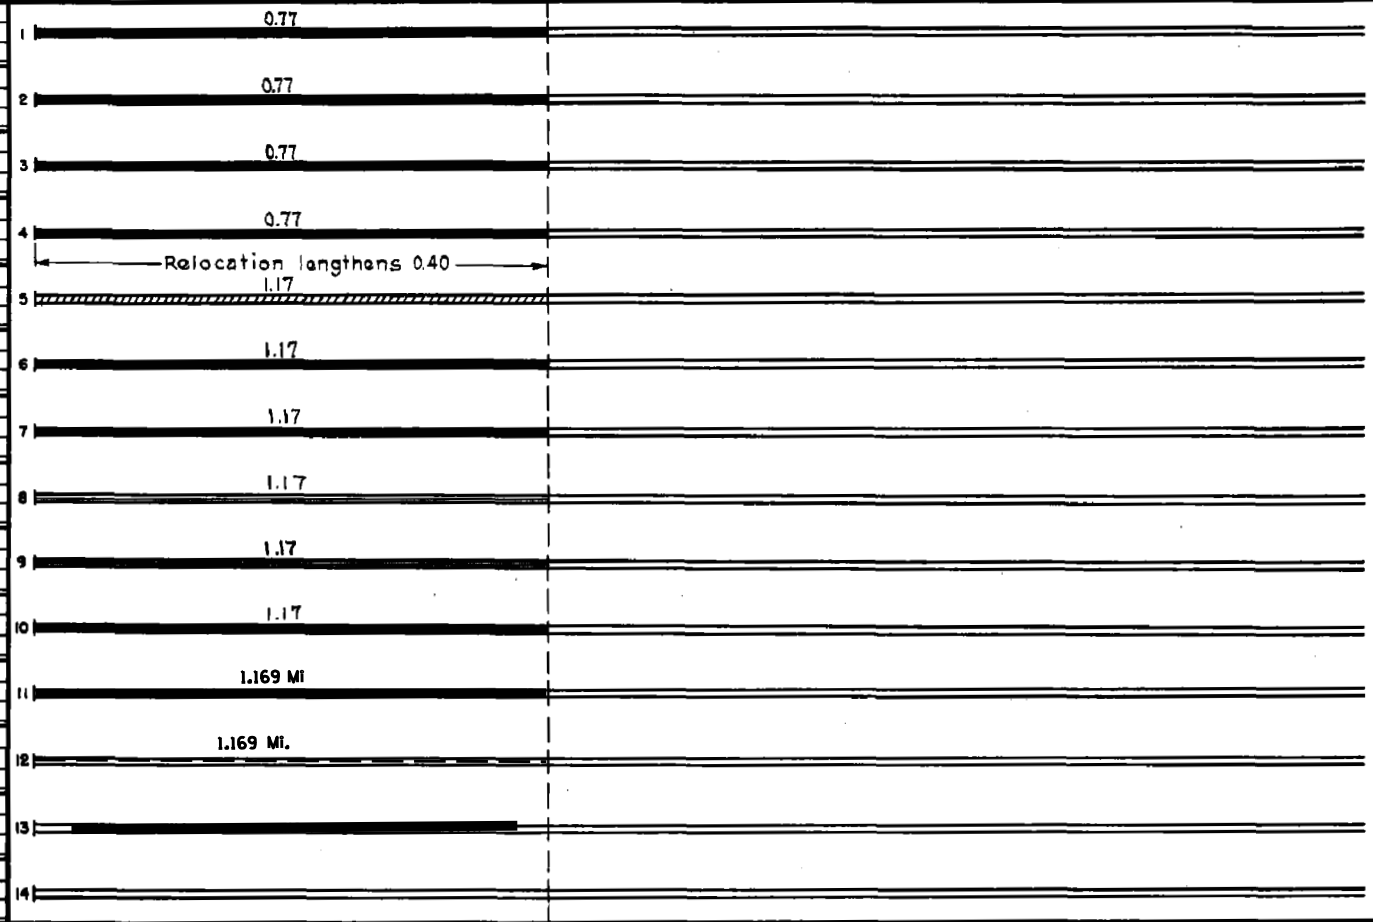

YEARS FROM TO	TOTAL MILES	UNINCORPORATED		INCORPORATED		RURAL		URBAN	
		RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.	RDWY. MI.	BR. MI.
1949 1952	0.77	0.77	0.00	0.00	0.00	0.77	0.00	0.00	0.00
1953	1.17	1.17	0.00	0.00	0.00	1.17	0.00	0.00	0.00

REMARKS: Layout is to scale as of 1949
