FORM R.L.-7 REV. 2-40

SHEET 1 OF 2

PREPARED BY
HIGHWAY PLANNING SURVEY
IN COOPERATION WITH
U. S. PUBLIC ROADS ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF HIGHWAYS
ROAD LIFE STUDIES
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1012
TRUNK HIGHWAY 212
COUNTY Carver
DISTRICT 5A & 8A

LIMITS: West Co. Line - Jct. T.H. 25

YEAR BUILT	PROJECT Nº	DESCRIPTION: TYPE	WIDTH	THICKNESS	REMARKS	CODE Nº
		Gravel	22-24'	1"-2"	No Record of Constr.	
1925	212-12-26-28	Grading	32'			
		Br. Nº 4557	27'		107' C.D.G.-O.H.	
1925	212-12-26-28	Gravel	26'	1"		
1925	212-12-26-28	Gravel	26'	2¼-3"	1478-1550 C.Y./Mile.	
1929	212-12-26-28	Concrete	20'	8-7-9		
M 1943	A.F.E.30	Grav. Shoulders			4' Rt. & Lt. 120 C.Y./Mi. Maint. Dept.	
C 1959	1012-01	Grading			Divided Highway	
	1012-01	Gravel Base			43110 Tons	
	1012-03	Br. 9318 & 9319	30'		9318 W.B. 9319 E.B.	
C 1959	1012-06	Gravel & Bit. Base			Divided Highway	
		Bit. Surf.	22'		272 Tons	
		Concrete	24'	8"		
C 1966	1012-05	Grading	47'		Const. of W.B. rdwy	
	1012-07	Gravel Sub-base & Base		5"	Divided Highway	
		P.C. Concrete	24'	9"		
C 1970	1012-09	Widening Concrete	4'	9"	E.B. Rdwy. Only	
		Asphaltic Concrete	24'	3"	Over P.C. Conc. Inp.	
		Bit. Shoulders			3' inside & 8' outside	
M 1971	SF	JOINT SEAL				
C 1976	1012-12	BIT. RECONSTRUCTION	22' & 24'	3/4"	WEAR COURSE 2361	
		DECK REPAIR		1" min.	LEVELING COURSE 2331	
		BR. 9318 & 9319				
C 1977	1012-14	CONC. PLANING &			W.B. ROADWAY ONLY	
	F012-2(48)	TEXTURING				
C 1982	1012-15	Bit. Resurfacing and Milling	2 @ 22' & 24'	1-2" 3/4"	Leveling # 2331 Weaving # 2361	
	F012-2(56)					

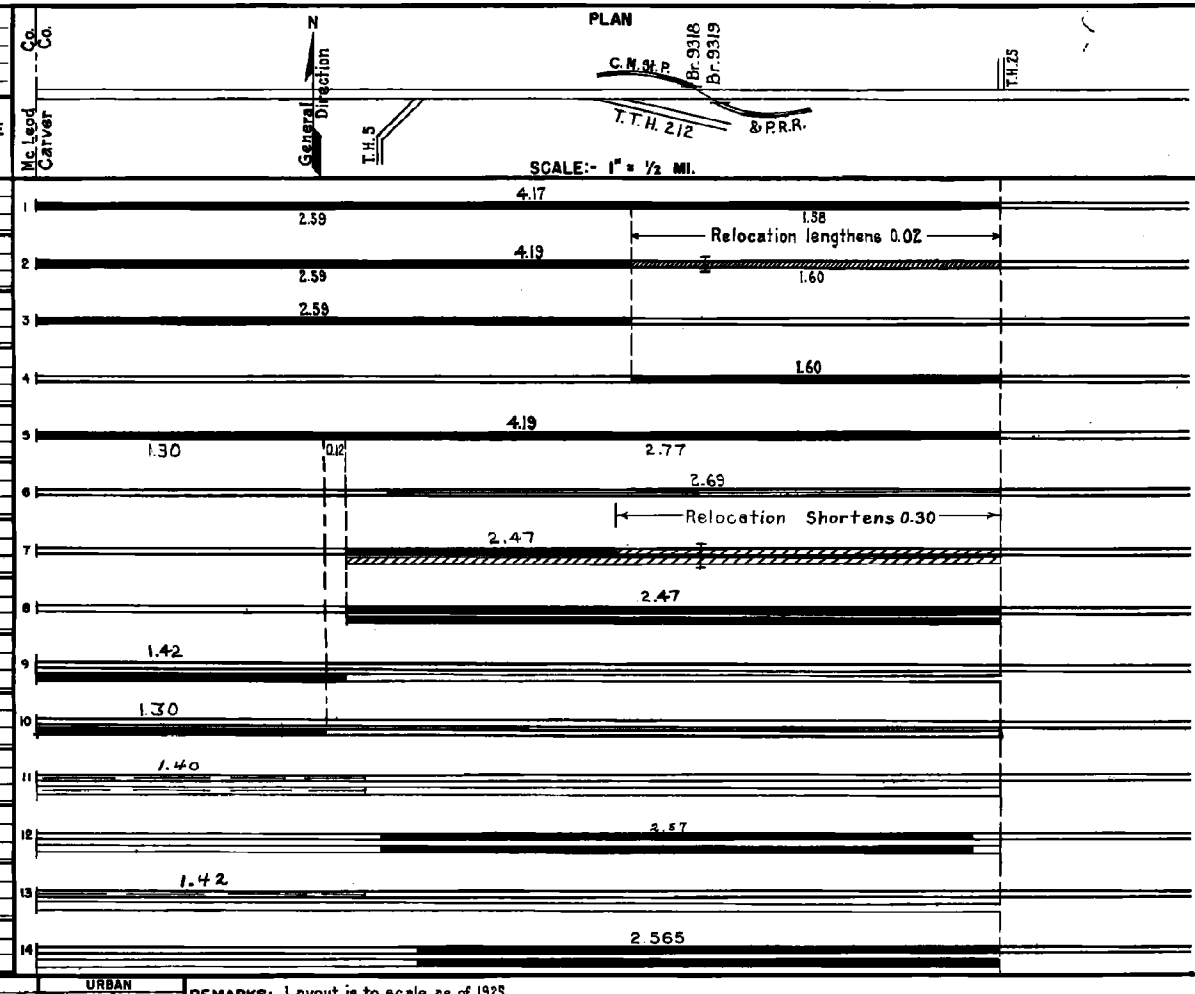

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.
1921	1924	4.17	3.47	0.00	0.70	0.00	4.17	0.00	0.00	0.00
1925	1958	4.19	3.34	0.03	0.42	0.00	4.16	0.03	0.00	0.00
1959		3.89	3.85	0.04	0.00	0.00	3.85	0.04	0.00	0.00

REMARKS: Layout is to scale as of 1925

FORM RL-7

PREPARED BY
BUREAU OF POLICY & PLANNING
IN COOPERATION WITH
U. S. DEPARTMENT OF TRANSPORTATION - FEDERAL HIGHWAY ADMINISTRATION

STATE OF MINNESOTA
DEPARTMENT OF TRANSPORTATION
CONSTRUCTION PROJECT LOG RECORD

CONTROL SECTION 1012
TRUNK HIGHWAY 212
COUNTY Carver
DISTRICT Metro & 8A

LIMITS: West Co. Line - Jct. T.H.25

Ref. Pt. 127+00.319 - 131+00.197



YEAR BUILT	PROJECT No	DESCRIPTION TYPE	WIDTH	THICKNESS	REMARKS
C					
1985	1012-16	Concrete Overlay	27′	7"	Bonded Overlay
		Bit. Overlay	24′	2½"	1½" 2331 , 1" 2341
M					
1989	M4338	Joint Repair			WB only
C					
1990	1012-18	Bridge Approaches			Grading & Surfacing at Br. 9318 & 9319
C					
1992	1012-19	Mill & Bit. Overlay	24′	1½-2"	Spec. 2331
				3½"	Spec. 2341
M					
2002	1012-22	Mill & Bit. Overlay	24′	1½"	Spec. 2350
S		Mill & Bit. Overlay;			
2003	1012-20	Drainage & Turn	24′	31/2"	Spec. 2360
		lane construction			
M					
2005	8825-198	Bit. Crack Seal			Spec. 2356
S		Grading, Mill & Unbonded	24′	9"	CO, 15′
2006	1012-21	Conc. O/L, Bit., Conc.,			Spec. 2360
		Turn La's , Culverts			EB only
S		Grading			
2013	1012-23	Bituminous Overlay	var	4.5"	Spec. 2360 WB only
		Turn La's			

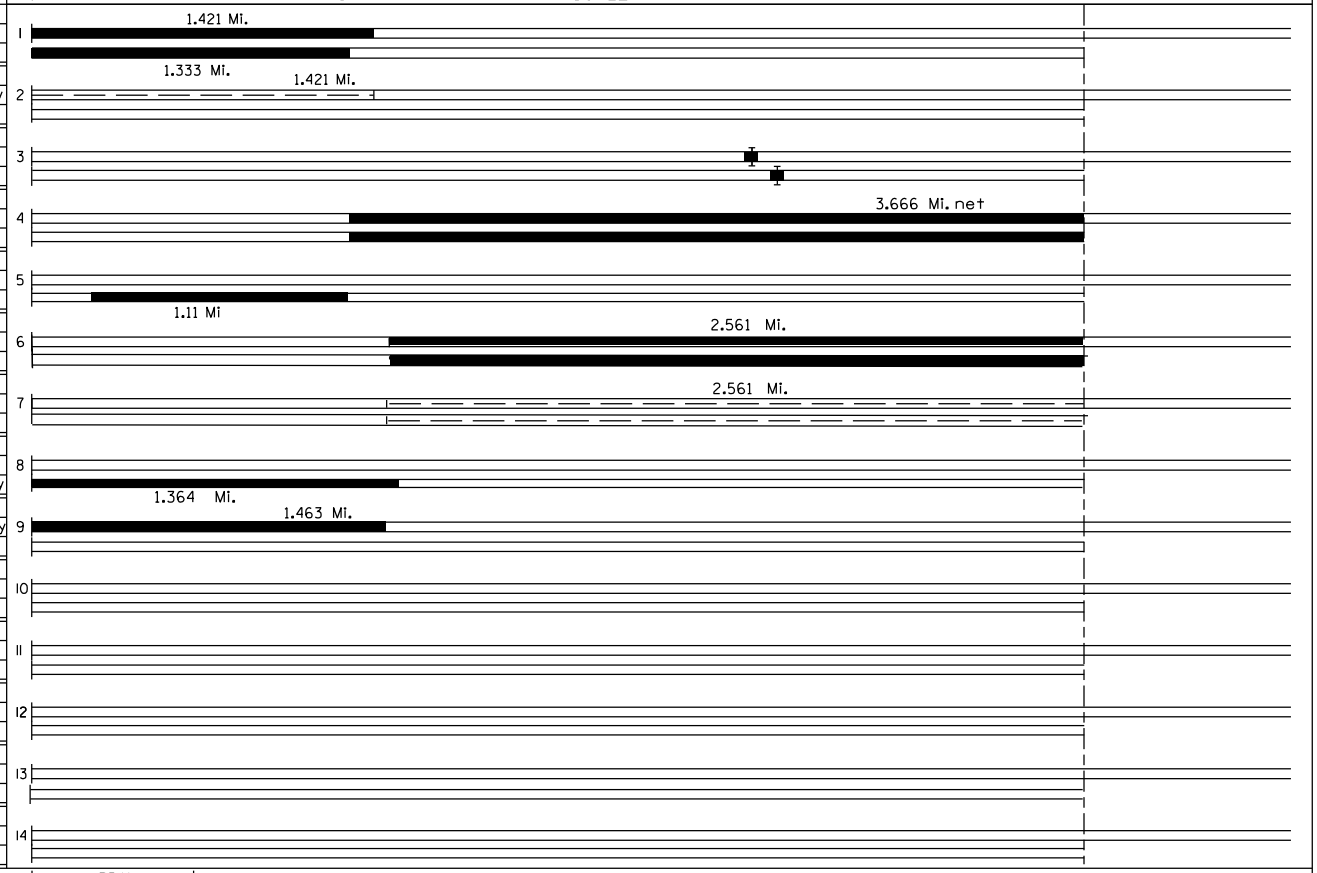

YEARS FROM	YEARS TO	TOTAL MILES	UNINCORPORATED RDWY. MI.	UNINCORPORATED BR. MI.	INCORPORATED RDWY. MI.	INCORPORATED BR. MI.	RURAL RDWY. MI.	RURAL BR. MI.	URBAN RDWY. MI.	URBAN BR. MI.

REMARKS:
